



Weekly Progress Report » Rockland School System » July 1, 2016

Recap of previous week's progress

- Final inspection of completed weatherization of all schools – FIM 2 building envelope improvements is substantially complete 6/28
- Weekly progress meeting with all contractors on site 6/28
- Tank Farm site location coordination with Siemens, Maritime, and RSU 13 – 6/28
- **Oceanside East**
 - ✓ Auditorium seating removed, staging in place for installation of ductwork and demo work
 - ✓ Ductwork in progress in classrooms
 - ✓ Boiler work ongoing
- **Oceanside West**
 - ✓ All equipment ordered - Airtemp
 - ✓ Boiler work ongoing
- **South School**
 - ✓ Reviewed plans on-site with Paul (Airtemp), Tim and Dewey (SMC), and Siemens energy team (engineering and service) for AC in administrative offices 6/28
 - ✓ Boiler work ongoing
- **Thomaston Grammar School**
 - ✓ Boiler work ongoing

Open Items:

- Determine accessibility to air handlers in additions at TGS and library unit at OHS West **Siemens/Scott Hall**
- Approve proposed OHS East AC equipment for Airtemp **Siemens**
- Review wall demo plans and move controls in TGS room 3 **Siemens**
- Finalize plans/equipment for AC in South School – reviewing wiring options 7/5 **Siemens/Airtemp**
- Determine playground schedule and layout at South **RSU 13/Siemens**
- Assign storage space at OHS West for Siemens' controllers **RSU 13/Scott Hall**
- Drain oil from tanks at South School **RSU 13/Scott Hall**
- Determine ship schedule for library ERV in OHS East for Airtemp **Siemens**



SIEMENS

Budget Review:

Oceanside East

Oceanside West

Rockland Middle School

South School


Thomaston Grammar



Photos:



Foam seal in OHS East main entry bulkhead

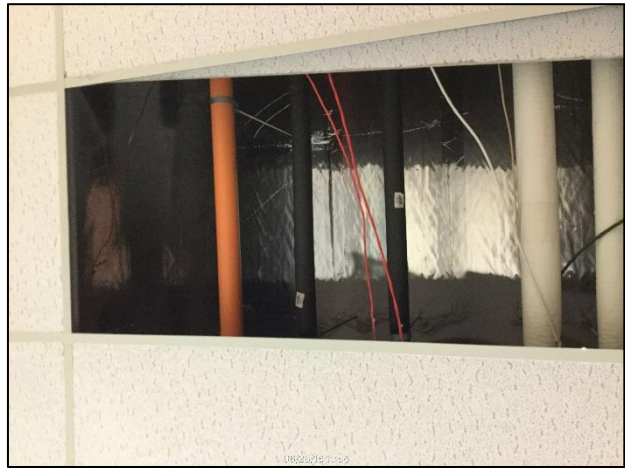

Air barrier in hallway at OHS West



Sealed above classroom vents in RDMS



Foam sealing in cafeteria at RDMS/South School




Weatherization of overhead door at OHS East



Foam above I-beam at OHS West main entrance




Weather stripping on exterior doors at RDMS and TGS

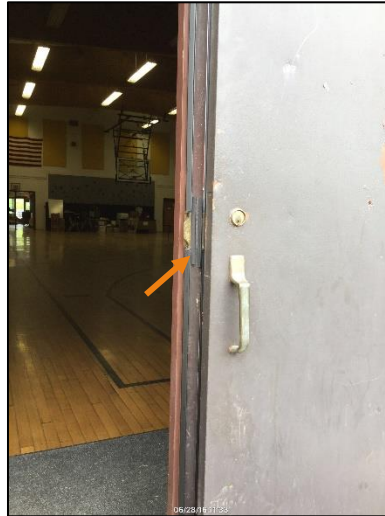

Weather sealing around windows



Pouring new slab for tanks in middle school boiler room

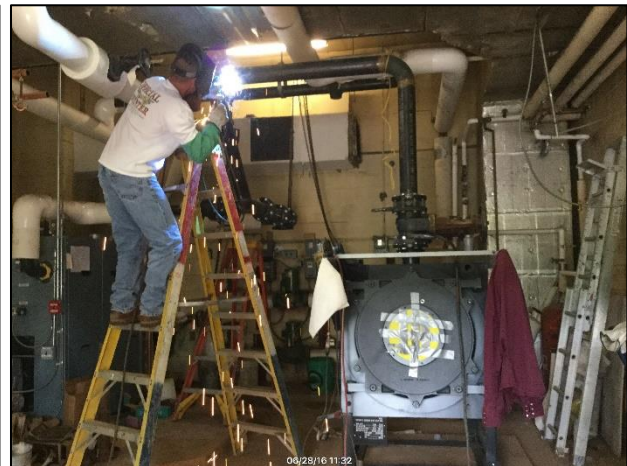

Installation of new boiler at TGS
