



Weekly Progress Report » Rockland School System » July 29, 2016

Oceanside East is now Oceanside High School (OHS); Oceanside West is now Oceanside Middle School (OMS); Rockland District Middle School is now South Elementary; South School is now South School Central Office (SSCO); Thomaston Grammar remains the same.

Recap of previous week's progress

- Weekly progress meeting with contractors on site – 7/26
- Meeting with representative from Viessmann to review boiler room piping in the middle school – 7/26
- New windows installed in the high school library and classroom 21
- Underground piping is installed at South Elementary
- Ductless split systems are being installed at the high school
- Sprinkler heads lowered at Oceanside Middle School
- Ductwork insulation ongoing at Oceanside Middle School
- Automatic isolation valves installed in the boiler rooms
- Ductwork ongoing throughout Oceanside HS and Oceanside MS

Open Items

- Confirming burner ship date **Siemens**

Budget Review

- Pay application 1 pending review
- Budget review meeting with RSU 13 – 8/2

Oceanside High School

Oceanside Middle School

South Elementary School

South School Central Office

Thomaston Grammar



Week ahead schedule update

Oceanside High School

- Portland Glass will be installing windows in the weight room 7/1-7/2 and along the back of the school 7/3-7/5
- SMC will continue work in the boiler room
- Airtemp has ductwork installations in the auditorium and continued work on the roof
- EMC will be receiving material and a second storage unit

Oceanside Middle School

- SMC will continue work in the boiler room
- Airtemp will be working on duct insulation throughout the building

South Elementary

- SMC will continue work in the boiler room

Thomaston Grammar

- SMC will continue work in the boiler room
- Airtemp will be in the library



SIEMENS

Photos:



Installation of underground piping at South Elementary School



New automated isolation valves are installed



Ductless splits are being installed




SIEMENS




New windows being installed at the high school



New windows being installed at the high school

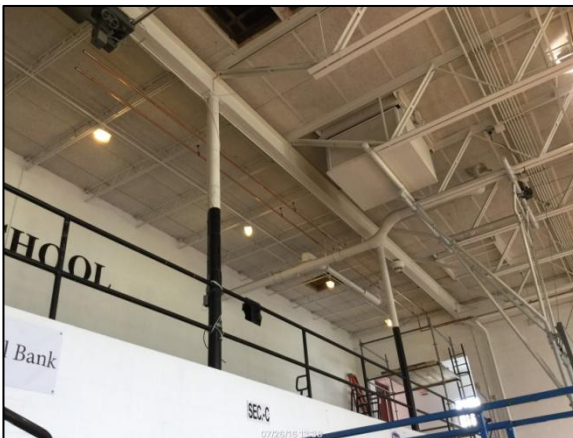

New piping in high school gym



Penetrations for piping at South Elementary




SIEMENS



Removal of overhead door and construction of exterior wall at Oceanside Middle School



Ductwork in hallway and auditorium

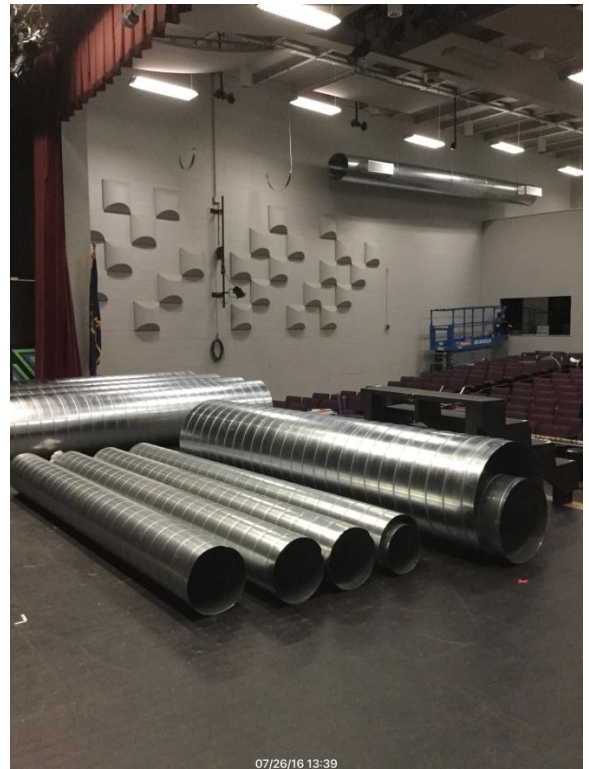

Prepared by Brian Rancourt and Sarah Huber
Please contact Sarah at sarah.huber.ext@siemens.com with corrections or additions
