



Weekly Progress Report » Rockland School System » July 8, 2016

Recap of previous week's progress

- Weekly progress meeting with contractors on site 7/5
- AC power wiring coordination meeting and walkthrough with Siemens, Paul (Airtemp), and J & J – 7/5
- **Oceanside East**
 - ✓ Ductwork in classrooms nearly complete
 - ✓ Boiler work ongoing
 - ✓ Boiler room slab for water tank complete and tank installed
 - ✓ Structural components for spiral ductwork installed in gym
 - ✓ AC equipment approved; installing week of 7/18
- **Oceanside West**
 - ✓ Boiler work ongoing
 - ✓ Electrical work ongoing
 - ✓ All equipment ordered for Airtemp to begin
- **South School**
 - ✓ Boiler work ongoing
 - ✓ AC power wiring plan determined
- **Thomaston Grammar School**
 - ✓ Boiler work ongoing
 - ✓ Pipe run complete through boiler room exterior wall to rear northeast corner of building

Open Items:

- Determine accessibility to air handlers in additions at TGS and library unit at OHS West **Siemens/Scott Hall**
- Assign storage space at OHS West for Siemens' controllers **RSU 13/Scott Hall**
- Drain oil from tanks at South School **RSU 13/Scott Hall**
- Determine ship schedule for library ERV in OHS East for Airtemp **Siemens**
- Review and move controls in TGS room 3 (wall demo now complete) **Siemens**
- Review options for replacing OHS East breaker **Siemens**
- Obtain purchase order numbers for Airtemp and SMC **Siemens/Mark Bednarski**
- Review pricing for AC in South School and OHS East **Siemens/J&J**
- Cut back shrubbery in front of windows where condensing units will be installed **RSU 13/Scott Hall**



SIEMENS

Budget Review:

Oceanside East

Oceanside West

Rockland Middle School

South School

Thomaston Grammar



Week ahead schedule update:

Oceanside East		Monday		Tuesday		Wednesday		Thursday		Friday	
		Start	End	Start	End	Start	End	Start	End	Start	End
Contractor →	SMC										
Area/Rooms →	Boiler Room	x	x	x	x	x	x	x	x	x	x
Contractor →	AirTemp										
Area/Rooms →	Roof - power wiring penetrations/curbs	x	x	x	x	x	x	x	x	x	x
	auditorium	x	x	x	x	x	x	x	x	x	x
	gym	x	x	x	x	x	x	x	x	x	x
	library	x	x	x	x	x	x	x	x	x	x
	classrooms	x	x	x	x	x	x	x	x	x	x

Oceanside West		Monday		Tuesday		Wednesday		Thursday		Friday	
		Start	End	Start	End	Start	End	Start	End	Start	End
Contractor →	SMC										
Area/Rooms →	Boiler Room	x	x	x	x	x	x	x	x	x	x
Contractor →	AirTemp										
Area/Rooms →	Ceilings/roofing/structural	x	x	x	x	x	x	x	x	x	x

South		Monday		Tuesday		Wednesday		Thursday		Friday	
		Start	End	Start	End	Start	End	Start	End	Start	End
Contractor →	SMC										
Area/Rooms →	Boiler Room	x	x	x	x	x	x	x	x	x	x

Thomaston Grammar		Monday		Tuesday		Wednesday		Thursday		Friday	
		Start	End	Start	End	Start	End	Start	End	Start	End
Contractor →	SMC										
Area/Rooms →	Boiler Room	x	x	x	x	x	x	x	x	x	x

Photos:




Pipe from boiler through exterior wall to corner of building - TGS




New extended slabs and water tank - South School boiler room



Installation of ductwork in OHS East classrooms is nearly complete

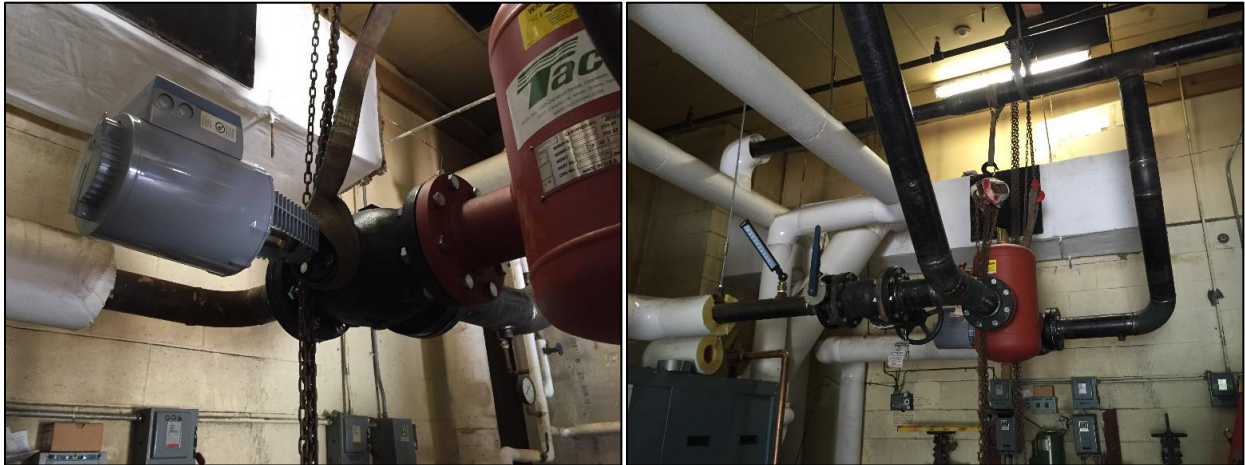

3-phase pumps installed in boiler rooms

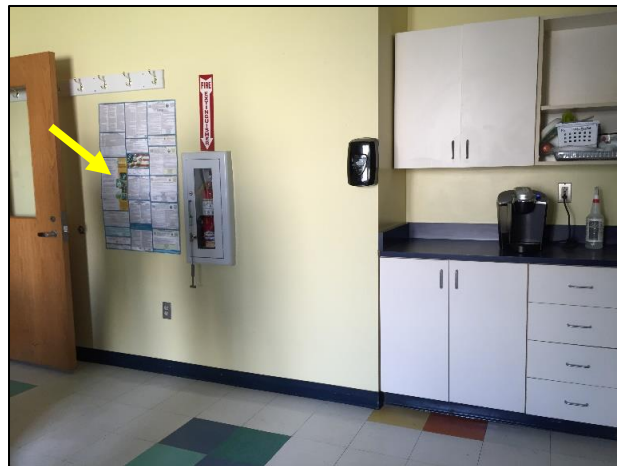

AC power wiring options investigated and location (indicated in photo) for new subpanel chosen – South School staff break room
